Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	02 October 2026
Team ID	SWTID-2026-9088
Project Name	Import Data using Transform Maps (Spreadsheet)
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation

The product backlog below follows the template structure and adapts the user stories to the documented employee spreadsheet import workflow. Story points use the planning scale used in the supplied planning logic.

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Data Preparation	USN-1	As an administrator, I can prepare the employee spreadsheet with the required source fields.	2	High	
Sprint-1	Data Preparation	USN-2	As an administrator, I can create the Employee Test target table for imported employee records.	3	High	
Sprint-1	Data Preparation	USN-3	As an administrator, I can create the Employee Import / Import Set staging table.	2	High	
Sprint-1	Transform Configuration	USN-4	As an administrator, I can create a Transform Map between Employee Import and Employee Test.	3	High	
Sprint-1	Transform Configuration	USN-5	As an administrator, I can map the source fields to the corresponding target fields.	3	High	
Sprint-2	Data Transformation & Validation	USN-6	As an administrator, I can run the transform and move employee data into Employee Test.	2	High	
Sprint-2	Data Transformation & Validation	USN-7	As an administrator, I can validate the transformed records and import results.	2	High	
Sprint-2	Data Transformation & Validation	USN-8	As an administrator, I can use Employee ID as Coalesce to prevent duplicate records.	3	High	
Sprint-2	Reporting & Dashboard	USN-9	As a user, I can view employee reports by department, location, and employee list.	3	Medium	
Sprint-2	Reporting & Dashboard	USN-10	As a user, I can view the Employee Analytics Dashboard containing the configured reports.	5	Medium	

Planned story points: Sprint 1 = 13 points; Sprint 2 = 15 points; Total = 28 points.


Project Tracker, Velocity & Burndown Chart

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	13	6 Days	02 Oct 2026	07 Oct 2026	To be updated	To be updated
Sprint-2	15	6 Days	08 Oct 2026	13 Oct 2026	To be updated	To be updated

Velocity

Planned team velocity = Total planned story points / Number of sprints
Total planned story points = 13 + 15 = 28
Number of sprints = 2
Planned velocity = 28 / 2 = 14 story points per sprint

Planned Burndown Chart

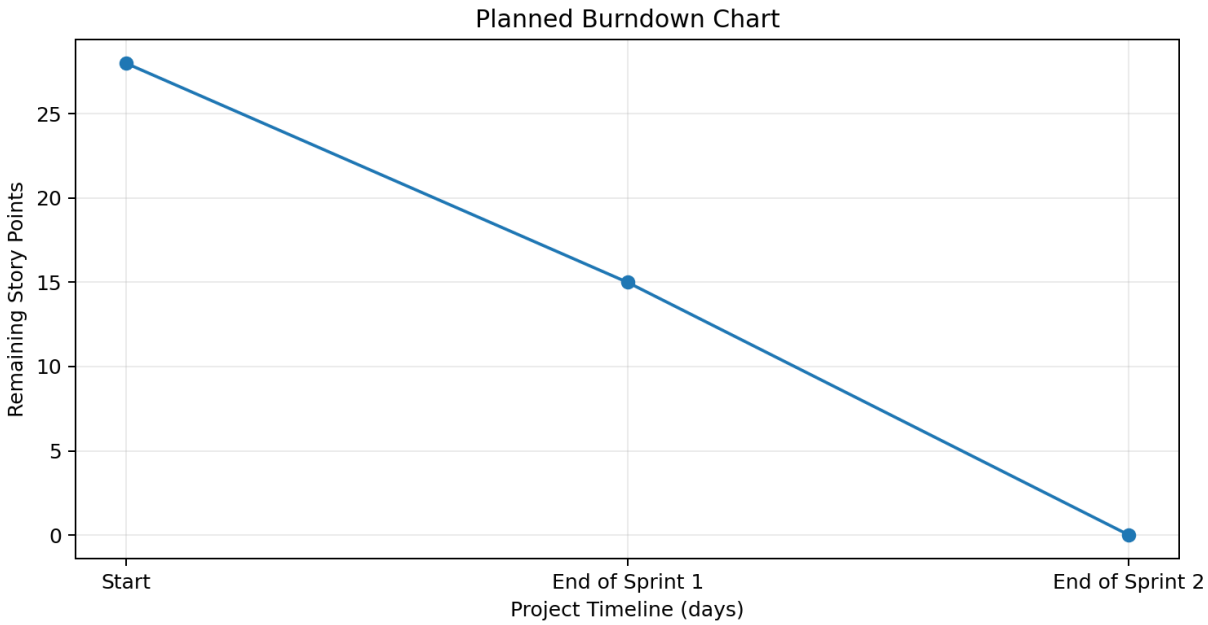

The burndown chart is a **planned** view because actual completed story points and actual release dates have not been supplied. It shows the intended reduction from 28 points at project start to 15 points after Sprint 1 and 0 points after Sprint 2 if all planned work is completed.

Planning Summary

Metric	Planned Value
Number of Sprints	2
Sprint Duration	6 Days each
Sprint 1 Points	13
Sprint 2 Points	15
Total Planned Story Points	28
Planned Velocity	14 Story Points / Sprint

Note: Team Members are left blank because the uploaded Project Planning Template requires that field but no team-member names were provided with this document. Actual completed points and actual release dates should be filled in after the corresponding sprint work is performed.
